

Department of Toxic Substances Control
Project Status Update
For
Wyle Laboratories Norco Facility Site
February 7, 2005

SITE INVESTIGATION/CLEANUP DOCUMENTS

- DTSC issued comments on the Draft Remedial Investigation Workplan on February 2, 2005. The Workplan, dated November 24, 2004, provides a detailed plan for the further assessment and characterization of chemicals in soil gas, soil, surface water, and ground water at the Wyle Labs site. The purpose of the RI is to define the nature and extent of Wyle-related contamination both onsite and in the surrounding community. This investigation includes the evaluation of bedrock fractures and offsite investigation near the northwestern boundary. The fracture analysis will help locate possible areas where contaminated groundwater may have migrated, and these areas can then be sampled.
- DTSC is reviewing the Revised Report of Additional Investigation Along Site Boundary dated December 22, 2004. The Report presents the results of the sampling conducted along the areas northwest, west, and southwest of the former Wyle Laboratories facility. The purpose of the Boundary Assessment was to determine whether Wyle related contaminants have impacted the surrounding community. Boundary sampling included soil, soil gas, surface water and groundwater along the boundaries of the site. Boundary sampling results revealed the presence of contamination near Wyle's northwestern boundary. Consequently, soil gas sampling was conducted along Golden West Lane and on residential properties.
- DTSC has received the revised schedule from Wyle. The Schedule was revised based on discussions with DTSC on January 27, 2005. The revised schedule is included as an attachment to this weekly update.


INVESTIGATION/CLEANUP FIELD WORK


- DTSC has requested Wyle to sample a seep in the backyard of a residence located on Raquel Road by February 11, 2005. Seep sampling procedure was submitted on January 27, 2005. DTSC requested modification to these procedures and re-submittal for DTSC review and approval prior to implementation.

PUBLIC PARTICIPATION:

- Responded to inquiries from legal representatives of the residence located at 998 3rd Street. TCE and Perchlorate were detected in the private well located on this property

RAW, RI, FS, RAP, RD, and RA Schedule Wyle Laboratories Norco, California																							Wed 2/2/05
ID	Task Name	Duration	Start	Finish	03		2004				2005				2006				2007				
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3						
1	SCOPING MEETING	0 days	Mon 11/10/03	Mon 11/10/03		◆ 11/10																	
2	Quarterly updates submitted to DTSC (IA, GW, VP, RP)	522 days	Fri 4/29/05	Mon 4/30/07																			
3	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 1	1 day	Fri 4/29/05	Fri 4/29/05																			
4	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 2	1 day	Fri 7/29/05	Fri 7/29/05																			
5	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 3	1 day	Mon 10/31/05	Mon 10/31/05																			
6	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 4	1 day	Mon 1/30/06	Mon 1/30/06																			
7	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 5	1 day	Mon 5/1/06	Mon 5/1/06																			
8	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 6	1 day	Mon 7/31/06	Mon 7/31/06																			
9	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 7	1 day	Mon 10/30/06	Mon 10/30/06																			
10	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 8	1 day	Mon 1/29/07	Mon 1/29/07																			
11	Quarterly updates submitted to DTSC (IA, GW, VP, RP) 9	1 day	Mon 4/30/07	Mon 4/30/07																			
12	REMOVAL ACTION WORKPLAN FOR GROUNDWATER	95 days	Wed 8/30/06	Tue 1/9/07																			
13	Wyle Prepares and Submits Removal Action Completion Report	45 days	Wed 8/30/06	Tue 10/31/06																			
14	DTSC reviews/comments on RAC Report	20 days	Wed 11/1/06	Tue 11/28/06																			
15	Wyle revises RAC Report	20 days	Wed 11/29/06	Tue 12/26/06																			
16	DTSC reviews/approves RAC Report	10 days	Wed 12/27/06	Tue 1/9/07																			
17	REMEDIAL INVESTIGATION	390 days	Mon 10/11/04	Thu 4/6/06																			
18	RI Workplan	98 days	Wed 11/24/04	Fri 4/8/05																			
19	Wyle submits Revised Draft RI Workplan	1 day	Wed 11/24/04	Wed 11/24/04																			
20	DTSC Comments on Offsite portions of RI Workplan	15 days	Wed 12/1/04	Tue 12/21/04																			
21	DTSC reviews and comments on complete Revised Draft RI Workplan	33 days	Wed 12/22/04	Fri 2/4/05																			
22	Wyle prepares RTC to all DTSC comments on entire RI Workplan	46 days	Fri 12/24/04	Fri 2/25/05																			
23	DTSC reviews and concurs on RTC	10 days	Mon 2/28/05	Fri 3/11/05																			
24	Wyle submits Final RI Workplan	10 days	Mon 3/14/05	Fri 3/25/05																			
25	DTSC approves final RI workplan	10 days	Mon 3/28/05	Fri 4/8/05																			
26	Field Activities	390 days	Mon 10/11/04	Thu 4/6/06																			
27	Off-Site Investigation	390 days	Mon 10/11/04	Thu 4/6/06																			
28	Private Well Survey	206 days	Tue 10/26/04	Mon 8/8/05																			
29	Wyle submits private well survey	15 days	Tue 10/26/04	Mon 11/15/04																			
30	DTSC distributes flyers	5 days	Mon 11/29/04	Fri 12/3/04																			
31	DTSC receives public responses	16 days	Mon 12/6/04	Mon 12/27/04																			
32	Wyle evaluates survey results	20 days	Tue 12/28/04	Mon 1/24/05																			
33	Follow up with private well users	5 days	Mon 1/31/05	Fri 2/4/05																			
34	Wyle prepares private well access agreements	11 days	Mon 1/31/05	Mon 2/14/05																			
35	Wyle prepares TM for private well sampling	6 days	Mon 2/7/05	Mon 2/14/05																			
36	DTSC reviews/comments TM	10 days	Tue 2/15/05	Mon 2/28/05																			
37	Wyle submits final TM	10 days	Tue 3/1/05	Mon 3/14/05																			
38	DTSC Approves TM	10 days	Tue 3/15/05	Mon 3/28/05																			
39	Wyle Samples private wells	10 days	Tue 3/29/05	Mon 4/11/05																			
40	Wyle submits draft private well sampling report	30 days	Tue 4/12/05	Mon 5/23/05																			
41	DTSC Reviews and comments on draft private well sampling report	10 days	Tue 5/24/05	Mon 6/6/05																			
42	Wyle finalizes and submits private well sampling report	10 days	Tue 6/7/05	Mon 6/20/05																			
Project: Wyle Project schedule Date: Wed 2/2/05		Task	<div></div>	Progress	<div></div>	Summary	<div></div>	External Tasks	<div></div>	External Milestone	◆	Deadline	↓										
		Split	<div></div>	Milestone	◆	Project Summary	<div></div>	External Milestone	◆	External Milestone	◆												
Carol Serlin Project Engineer																							Matt Letany Project Coordinator

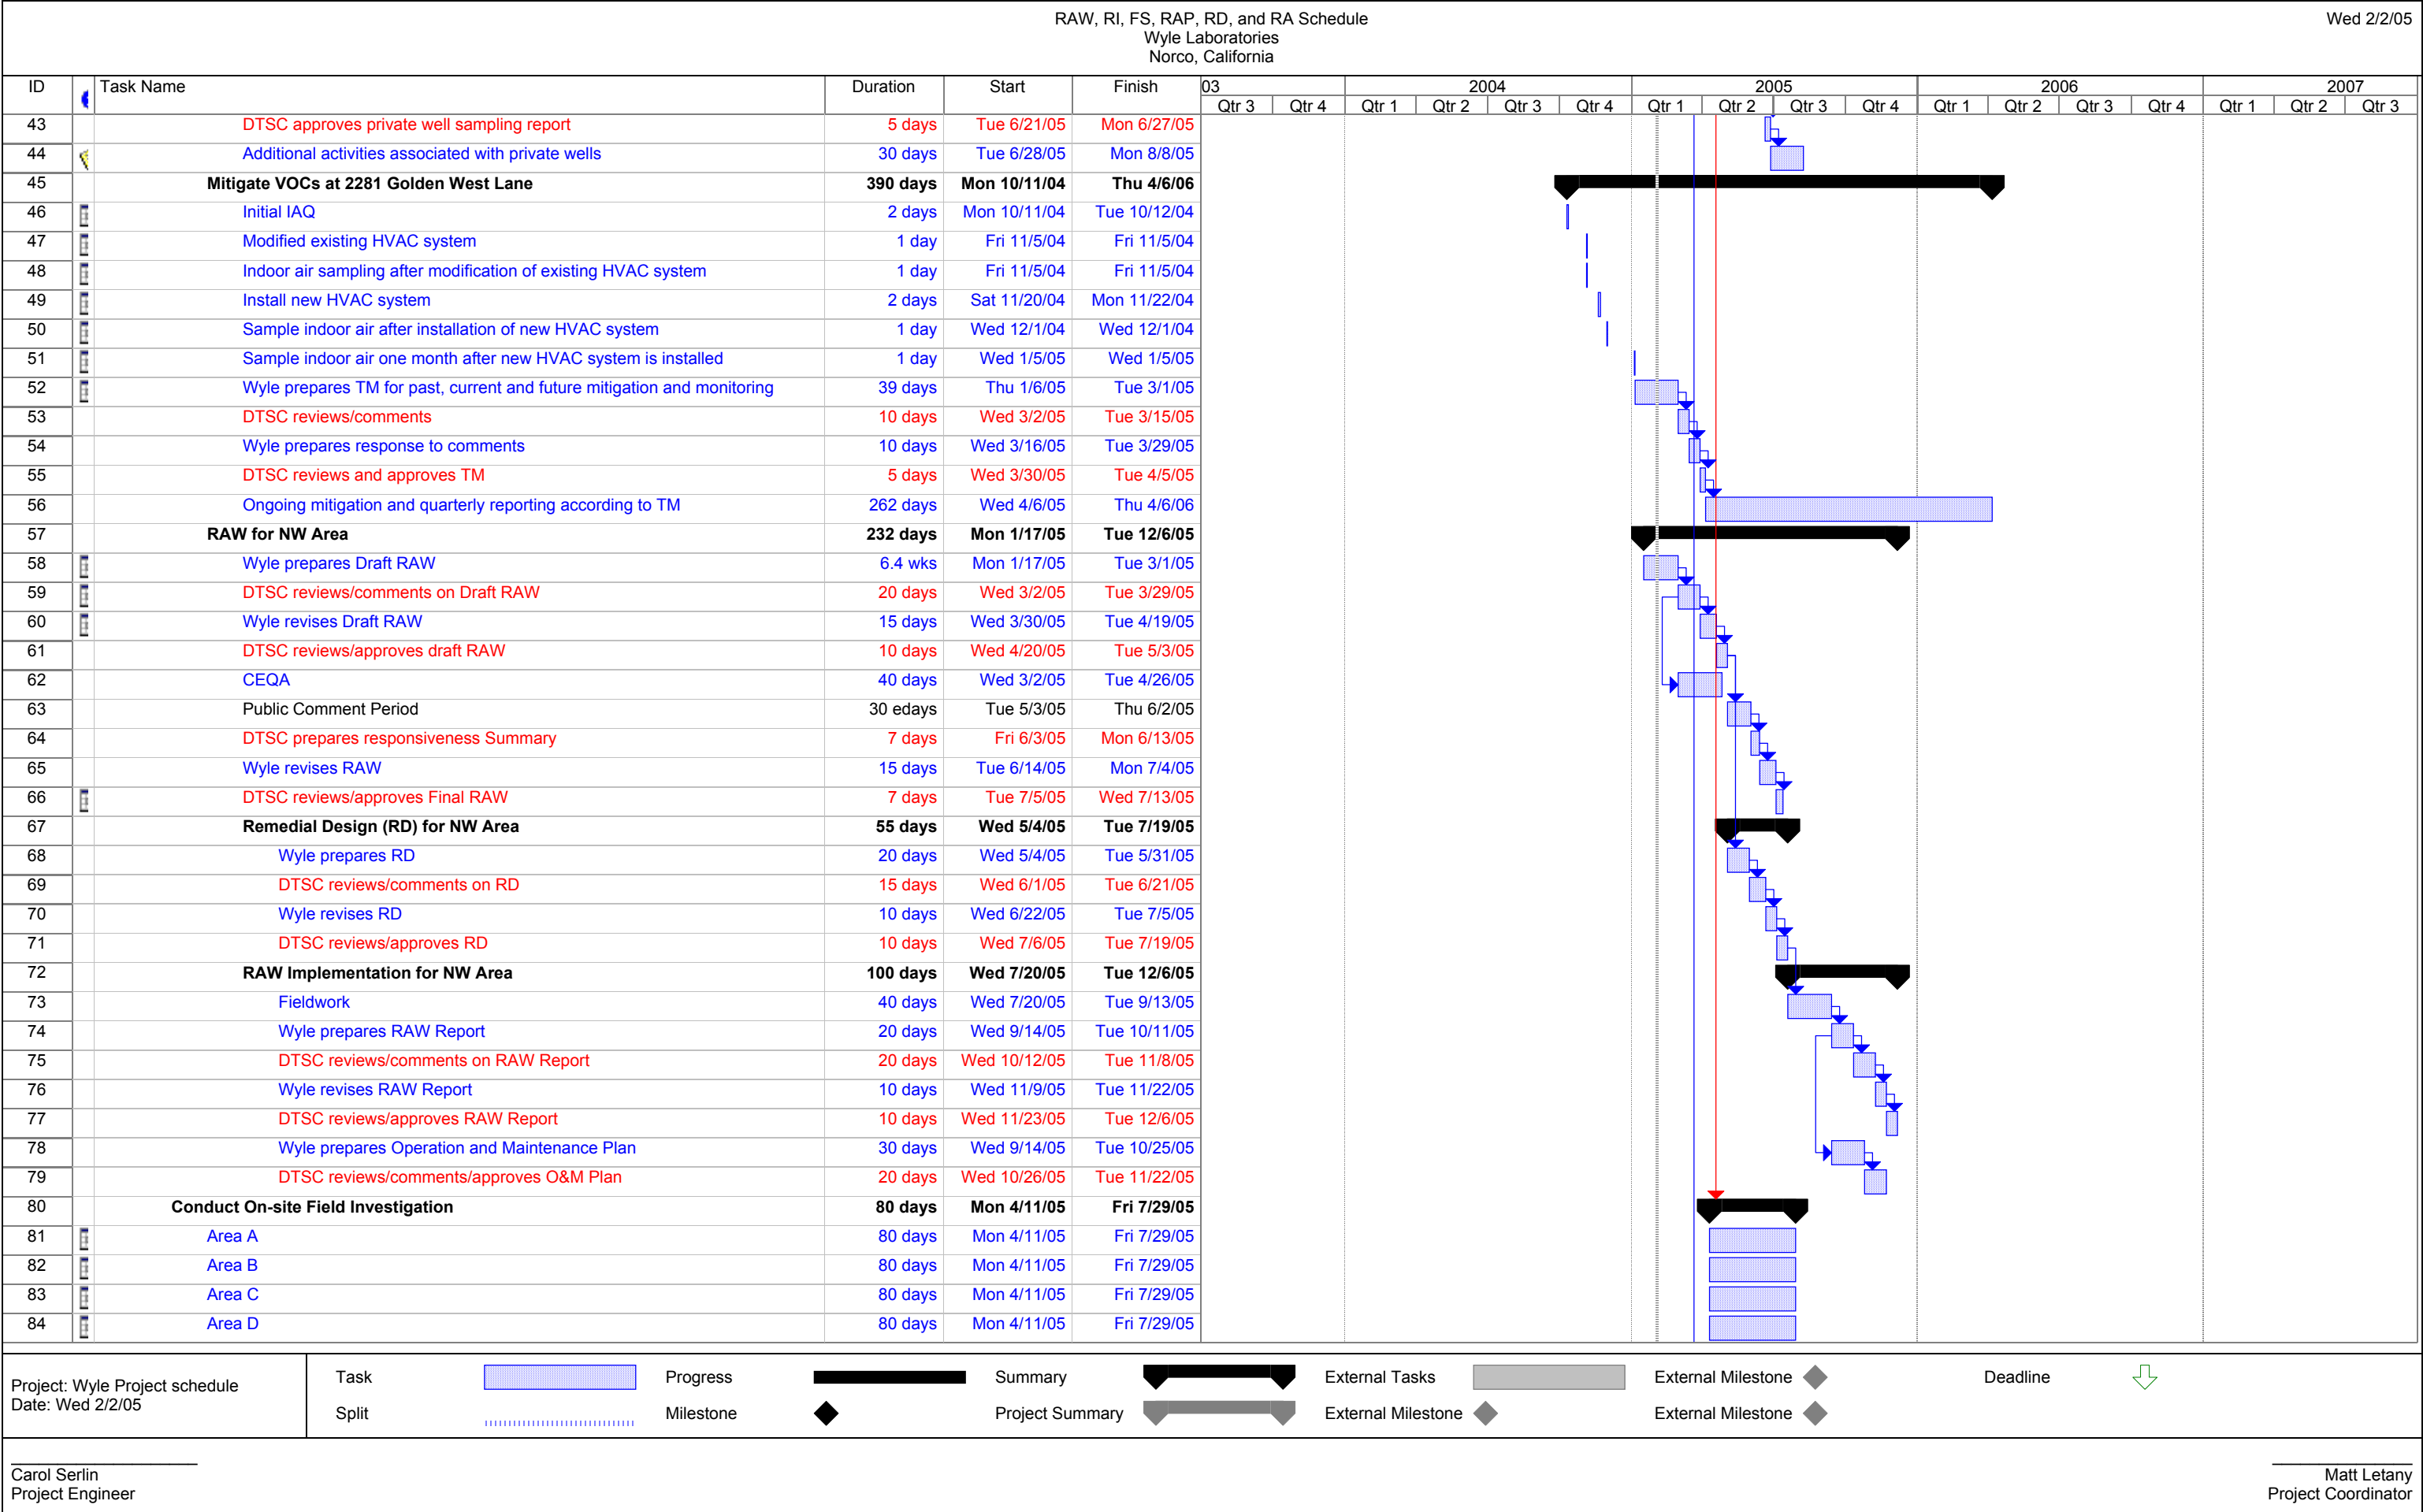

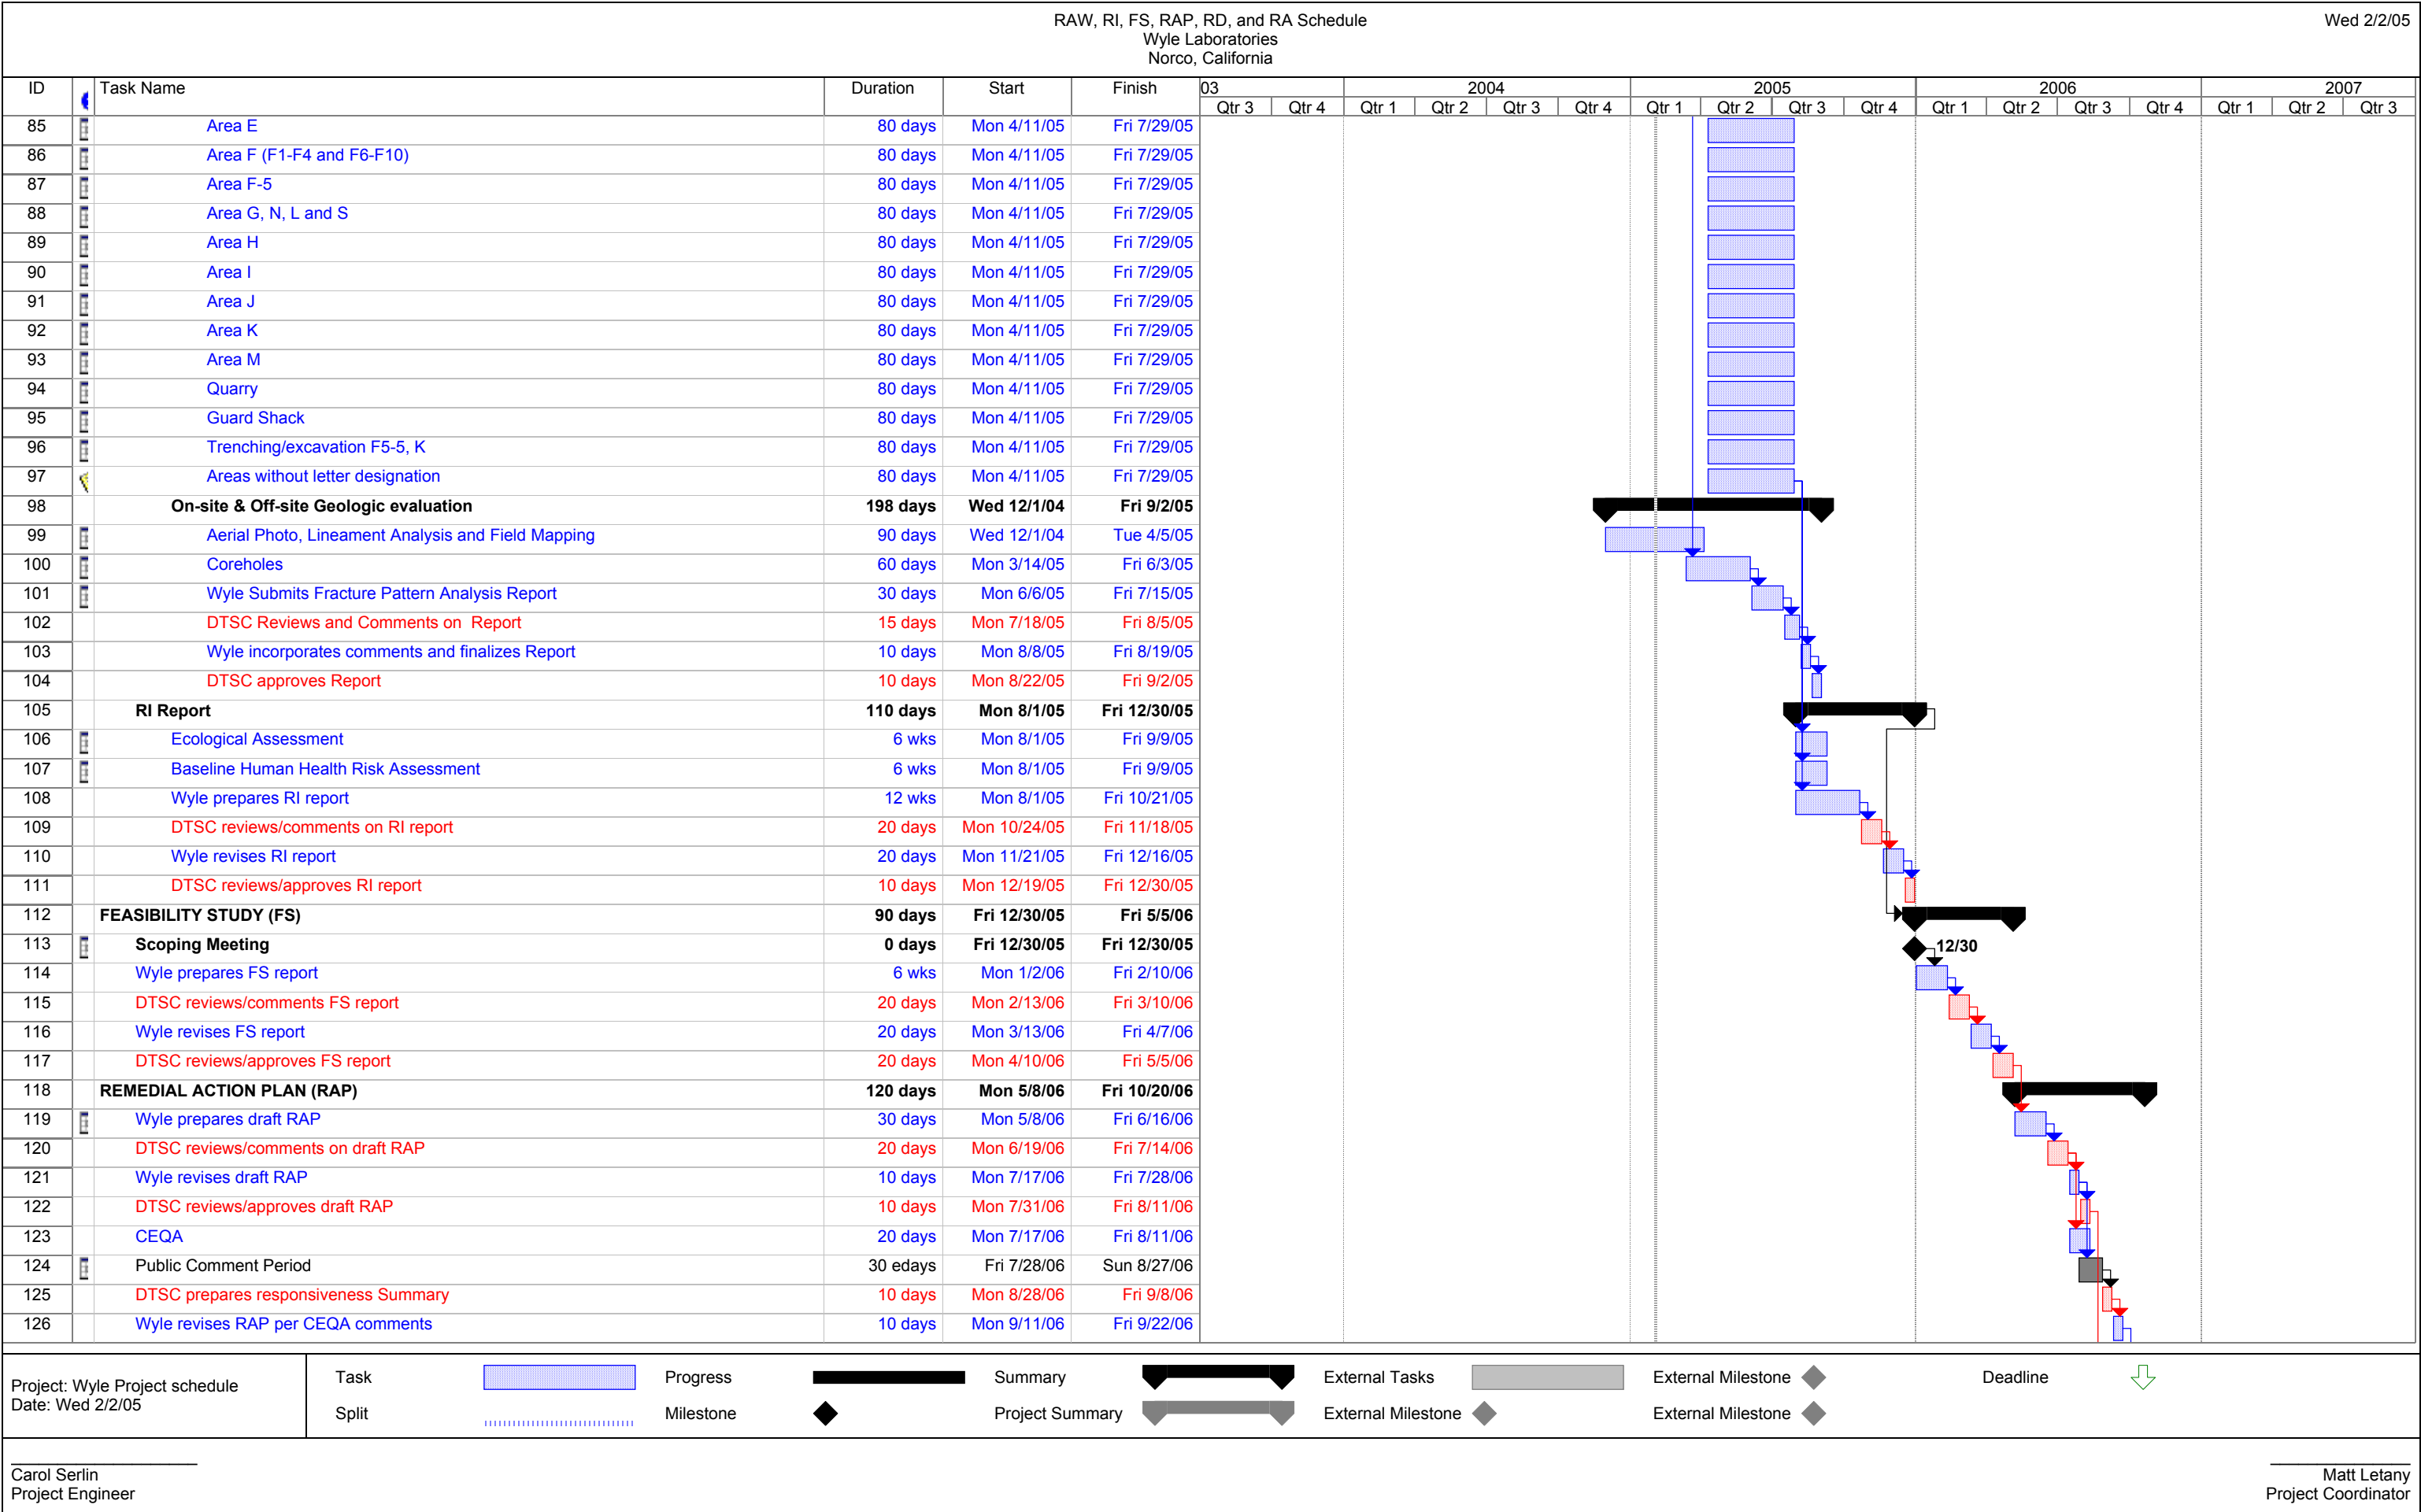

RAW, RI, FS, RAP, RD, and RA Schedule
Wyle Laboratories
Norco, California

Wed 2/2/05

ID	Task Name	Duration	Start	Finish	03	2004				2005				2006				2007			
					Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
127	DTSC approves RAP	20 days	Mon 9/25/06	Fri 10/20/06																	
128	Remedial Design (RD)	100 days	Mon 8/14/06	Fri 12/29/06																	
129	Wyle prepares RD	60 days	Mon 8/14/06	Fri 11/3/06																	
130	DTSC reviews/comments on RD	20 days	Mon 11/6/06	Fri 12/1/06																	
131	Wyle revises RD	10 days	Mon 12/4/06	Fri 12/15/06																	
132	DTSC reviews/approves RD	10 days	Mon 12/18/06	Fri 12/29/06																	
133	Remedial Action (RA)	100 days	Mon 1/1/07	Fri 5/18/07																	
134	Fieldwork	40 days	Mon 1/1/07	Fri 2/23/07																	
135	Wyle prepares RA report	20 days	Mon 2/26/07	Fri 3/23/07																	
136	DTSC reviews/comments on RA report	20 days	Mon 3/26/07	Fri 4/20/07																	
137	Wyle revises RA	10 days	Mon 4/23/07	Fri 5/4/07																	
138	DTSC reviews/approves RA report	10 days	Mon 5/7/07	Fri 5/18/07																	
139	ESTIMATED END PROJECT DATE	0 days	Fri 5/18/07	Fri 5/18/07																	5/18

Project: Wyle Project schedule
Date: Wed 2/2/05

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

External Milestone

External Milestone

Deadline

Carol Serlin
Project Engineer

Matt Letany
Project Coordinator
